[Future State] GCP Instances Strategy

Last updated by | Vessela Velinova-Slancheva | Feb 23, 2026 at 4:55 PM GMT+2

Post GCP migration Promo+ instance strategy has to align with the C4P one as depicted below:

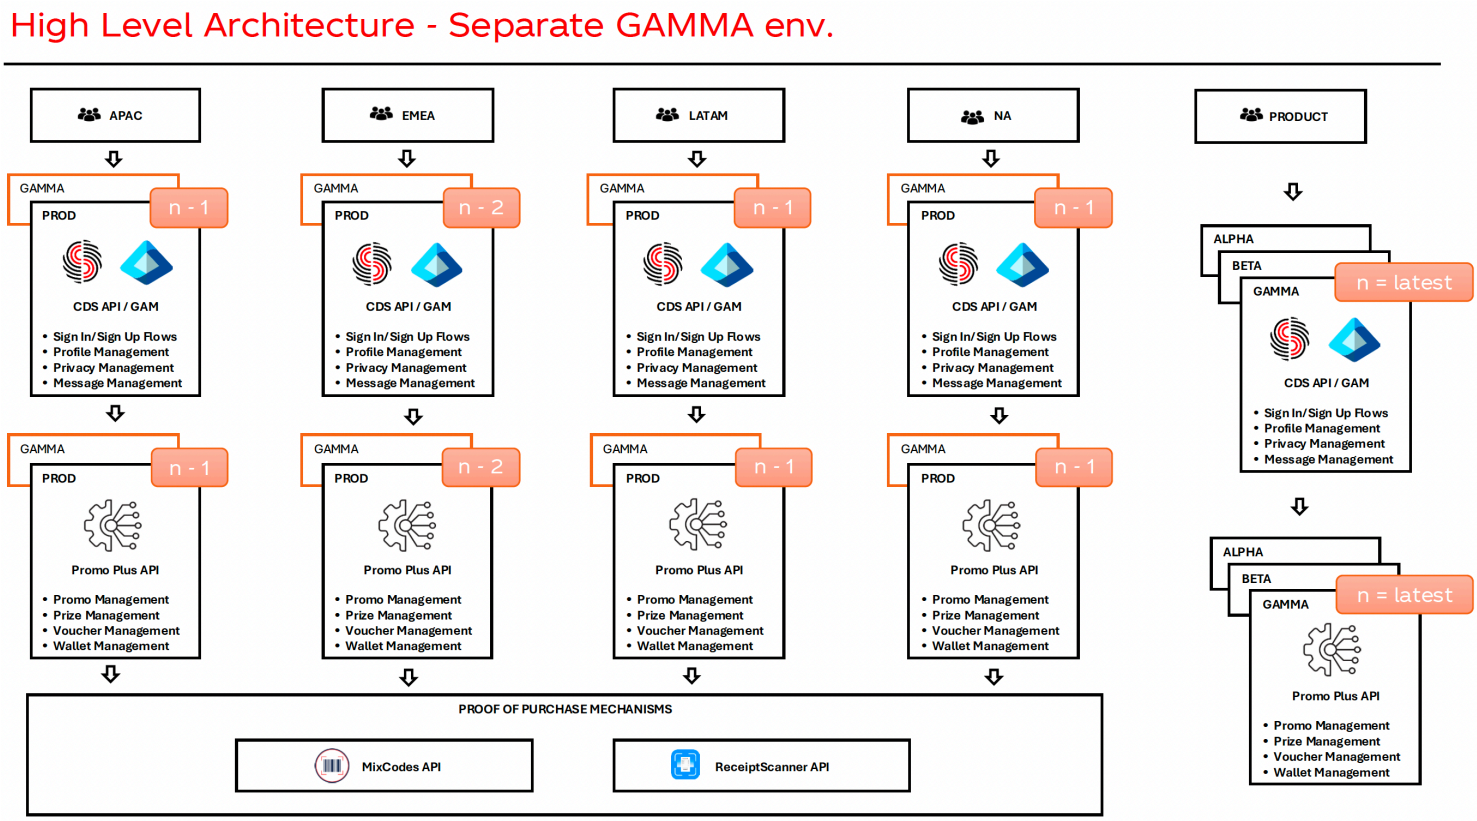

The evolution of the activation & support models for global charters/promotions based on the Regional Ops teams services allows splitting to regional instances and deprecating the Global instance post-migration. OneXP as the single client of the Global instance will integrate to all four of the regional instances and run the promotions against the regional instance for the respective markets (sites).

Proposed Split

Experience	Currently Hosted	Future State
OneXP Promotions APAC, NAOU, LATAM, EME	Global instance	**Regional instances**
OneXP Promotions EU	EMEA instance	EMEA instance
CCA & Daha Daha	EMEA instance	EMEA instance
Italy Promotions	Italy instance	Italy instance
NAOU Promotions	Global instance	**NAOU instance**
LATAM Regional Experience Promotions	LATAM instance	LATAM instance
APAC Regional Experience Promotions	APAC instance	APAC instance

Risks and Mitigation

Risk Area	Risk Description	Mitigation / Control	Owner
OneXP Integration	Dependency on the OneXP team to complete the reconfiguration for all remaining markets	Communicate, track and validate end-to-end per region before Global sunset	OneXP Team (Prabhu)
Regional Readiness	Regions may not be fully prepared to operate Promo+ in Production independently	Define and enforce readiness gates (Ops sign-off, monitoring, on-call, deployment validation) before redirecting traffic	Operations (Daniel)
Operational Ownership	Unclear incident ownership once Global Promo+ instance is no longer live	Publish updated RACI including the new scope for Regional Ops, Global Ops, and Promo+	MarTech Leadership (Tanya)
Hidden Dependencies	Legacy services or experiences may still reference Global Promo+ endpoints; Old integration dependencies (ex wallet, points)	Perform dependency audit and freeze new Global usage; monitor for unexpected Global calls; migrate old wallets	Promo+ (Vessela) / Operations (Daniel)
Active Campaigns	Campaigns may still be running on Global at the time of sunset	Execute phased sunset: freeze new launches → expire active campaigns → redirect traffic → decommission	Promo+ / Operations (Vessela / Daniel)
Escalation Surge	Increase in incidents and escalations during the transition period	Introduce a temporary hypercare phase with clear escalation thresholds and response SLAs	Operations (Daniel)
Market Confusion	Markets may be unclear where to launch or operate promotions post-sunset	Issue clear market communication outlining “What changes / What stays the same”	Promo+ (Vessela)
Analytics	Flows being sent to CX teams; multiple sources	Define what data is where; update the mapping; patterns of consumption	Promo+ (Vessela)

Sunset Readiness Gate

Global Promo+ can be fully sunset **only when all of the following are true**:

- OneXP routes 100% of promotion traffic to regional instances
- No active campaigns are running on Global
- Ops team confirm Production readiness (on-call, monitoring, deployments)

- No critical dependencies on Global Production remain

Next Steps to Align On (23-Feb)

- [ ] Formalise the role of the Global Promo+ instance - repurposing to NAOU instance or sunsetting entirely while creating a new NAOU instance
- [ ] Confirm Regional instance ownership & accountability
- [ ] Define the sunset milestone

Operational Follow-ups:

- [ ] Create a RACI on a high-level & Regional owners - Tanya & Vessela & Daniel
- [ ] Explicit ownership assignment for OneXP changes - Prabhu
- [ ] Update support and escalation model - Daniel
- [ ] Create a phased sunset timeline - Vessela
